

Haid Fire

1419 Harrison Ave, PC FL. 32401
Phone (850)238-1908

Fire Alarm
Annual Inspection Report
Service Date: 3/27/2025

JOB LOCATION:

Dunes Of Panama / BLDG A
7205 Thomas Dr.
Panama City Beach, FL 32408

CLIENT:

Same

CONTACT:

TECHNICIAN:

David Haid

Num: 1
Location: ELECTRICAL ROOM
Manufacturer: Firelite
Model #: ES-200X
Monitoring Agency: DYNAMARK ACC# 691-8538
Install Date:
Last Service: 4/2025
Serial #:
Bar Code:
Timestamp:

Remarks: THE FOLLOWING NOTES WERE MADE DURING THE ANNUAL FIRE ALARM INSPECTION AND TESTING:

1. FACP WAS SYSTEM ALL NORMAL UPON ARRIVAL. (SEE EXHIBIT 3.)
3. BOTH FACP BATTERIES PASSED LOAD TESTING (SEE EXHIBIT 4 & 5)
4. ALL COMMUNICATION SIGNALS WERE VERIFIED THROUGH THE MONITORING AGENCY.
5. THE PANEL WAS RETURNED TO NORMAL AND TAGGED UPON COMPLETION OF INSPECTION AND TESTING. (SEE EXHIBIT 6)

Initiating Devices

Num	Location	Type	Mfg	Install	Service	Bar Code	Timestamp
1	1ST FLOOR EAST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
2	1ST FLOOR EAST	Horn/Strobe	System Sensor		Annual 3/2025		*** Passed ***
3	1ST FLOOR CENTER	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
4	1ST FLOOR CENTER	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
5	1ST FLOOR WEST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
6	1ST FLOOR WEST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
7	2ND FLOOR EAST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
8	2ND FLOOR EAST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
9	2ND FLOOR CENTER	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
10	2ND FLOOR CENTER	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
11	2ND FLOOR WEST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
12	2ND FLOOR WEST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
13	3RD FLOOR EAST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
14	3RD FLOOR EAST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
15	3RD FLOOR CENTER	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
16	3RD FLOOR CENTER	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***

Haid Fire

JOB LOCATION:
 Dunes Of Panama / BLDG A

CLIENT:
 Same

Num	Location	Type	Mfg	Install	Service	Bar Code	Timestamp
17	4TH FLOOR EAST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
18	3RD FLOOR WEST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
19	4TH FLOOR EAST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
20	3RD FLOOR WEST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
21	4TH FLOOR CENTER	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
22	4TH FLOOR CENTER	Horn	System Sensor		Annual 3/27/2025		*** Passed ***
23	4TH FLOOR WEST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
24	4TH FLOOR WEST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
25	5TH FLOOR EAST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
26	5TH FLOOR EAST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
27	5TH FLOOR CENTER	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
28	5TH FLOOR CENTER	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
29	5TH FLOOR WEST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
30	5TH FLOOR WEST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
31	6TH FLOOR EAST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
32	6TH FLOOR EAST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
33	6TH FLOOR CENTER	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
34	6TH FLOOR CENTER	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
35	6TH FLOOR WEST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
36	6TH FLOOR WEST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
37	7TH FLOOR EAST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
38	7TH FLOOR EAST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
39	7TH FLOOR CENTER	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
40	7TH FLOOR CENTER	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
41	7TH FLOOR WEST	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
42	7TH FLOOR WEST	Horn/Strobe	System Sensor		Annual 3/27/2025		*** Passed ***
43	GROUND FL FRONT EXIT	Pull Station	Firelite		Annual 3/27/2025		*** Passed ***
44	ABOVE FACP	Heat Detector	System Sensor		Annual 3/27/2025		*** Passed ***

Haid Fire

JOB LOCATION:
Dunes Of Panama / BLDG A

CLIENT:
Same

Num	Location	Type	Mfg	Install	Service	Bar Code	Timestamp
45	ELECTRICAL ROOM	Heat Detector	System Sensor		Annual 3/27/2025		*** Passed ***
46	ELEVATOR EQUIPMENT RM	Heat Detector	System Sensor		Annual 3/27/2025		*** Passed ***
47	UTILITY/STORAGE ROOM	Heat Detector	System Sensor		Annual 3/27/2025		*** Passed ***
48	ABOVE FACP	Smoke Detect.	Firelite		Annual 3/27/2025		*** Passed ***
49	GROUND FL ELEV LANDING	Smoke Detect.	Firelite		Annual 3/27/2025		*** Passed ***
50	1ST FL ELEVATOR LANDING	Heat Detector	Firelite		Annual 3/27/2025		*** Passed ***
51	2ND FL ELEVATOR LANDING	Heat Detector	Firelite		Annual 3/27/2025		*** Passed ***
52	3RD FL ELEVATOR LANDING	Heat Detector	Firelite		Annual 3/27/2025		*** Passed ***
53	4TH FL ELEVATOR LANDING	Heat Detector	Firelite		Annual 3/27/2025		*** Passed ***
54	5TH FL ELEVATOR LANDING	Heat Detector	Firelite		Annual 3/27/2025		*** Passed ***
55	6TH FL ELEVATOR LANDING	Heat Detector	Firelite		Annual 3/27/2025		*** Passed ***
56	7TH FL ELEVATOR LANDING	Heat Detector	Firelite		Annual 3/27/2025		*** Passed ***
57	IN FACP	Battery	12V 7AH		Annual 3/27/2025		*** Passed ***
58	IN FACP	Battery	12V 7AH		Annual 3/27/2025		*** Passed ***
59	IN FACP	Communicator	M2M		Annual 3/27/2025		*** Passed ***

Tests and Maintenance

I. Annual

1. Alarm indicating appliances (visual and audible) were tested and are operational. OK
2. The primary power supply was tested and is operational. OK
3. The secondary power supply was tested and is operational. OK
4. The lamp and LED circuits were tested and are satisfactory. OK
5. Smoke detectors were recalibrated and operate satisfactorily. OK
6. Batteries were discharged for two hours and remain operational. OK
7. Battery charging devices were tested for proper operation. OK
8. Battery voltage was measured under full load with charger disconnected. OK
9. The meters for monitoring the power supply adequacy in telegraphic fire alarm systems were recalibrated and are accurate. NA
10. Batteries had the float voltage measured in each cell and are satisfactory. OK
11. Bell or horns were tested and are operational. OK
12. Annunciators were tested and are operational. NA
13. Control units were tested and all functions are operational. OK
14. Voice alarm system components were tested and are operational. NA
15. Each initiating and signaling circuit was tested for trouble signs. OK

I state that the information on this form is correct at the time and place of my inspection. And that all equipment tested at this time was left in operational condition upon completion of this inspection except as noted above.


Haid Fire

JOB LOCATION:

Dunes Of Panama / BLDG A


CLIENT:

Same



Technician David Haid
4/2/2025 11:06:15 AM

Accepted By




1. FASA: DAVID HAID

2. FASA: GARRET VANTREASE

Haid Fire

JOB LOCATION:
Dunes Of Panama / BLDG A

CLIENT:
Same

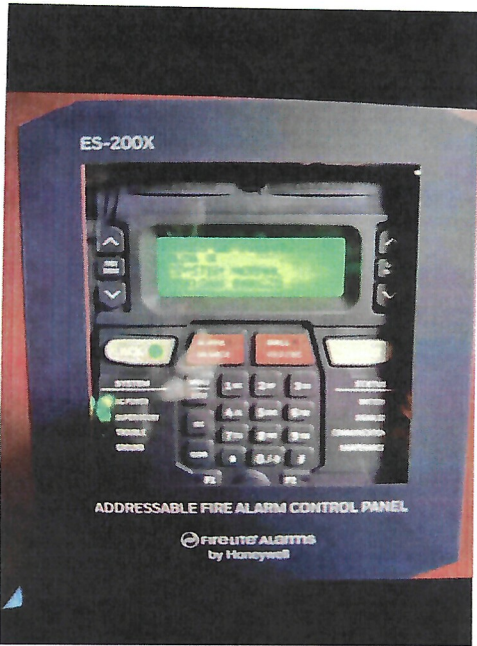


3. FACP UPON ARRIVAL



4. FACP BATT#1(02/2024)GOOD



5. FACP BATT#2(02/2024)GOOD

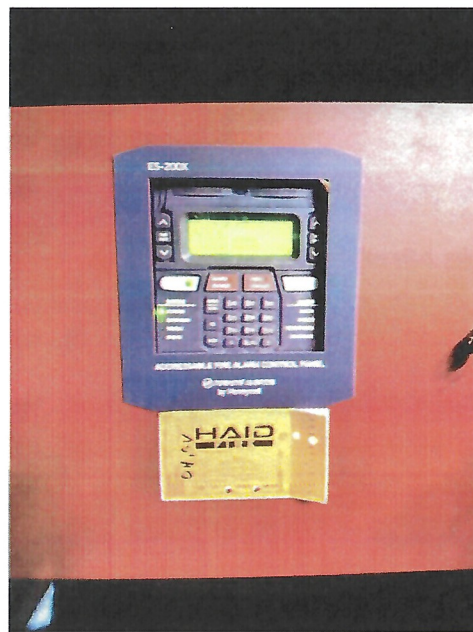

6. FACP UPON COMPLETION

*** End of Report ***
